


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2						
								T	W	T	F	S		
1		City of Nevada 40x60 PEMB	74 days	Tue 8/9/22	Fri 11/18/22									
2		Building Engineering	12 days	Tue 8/9/22	Wed 8/24/22									
3		Drawing approvals	5 days	Tue 8/9/22	Mon 8/15/22									
4		Pier/OH Beam/Cat walk engineering	5 days	Thu 8/18/22	Wed 8/24/22	3FS+2 days								
5		Concrete & Excavation	10 days	Thu 9/8/22	Wed 9/21/22									
6		dig piers set steel - steel & anchor bolts due at start	2 days	Thu 9/8/22	Fri 9/9/22	4FS+10 days	J&L Contractor							
7		Pour piers	1 day	Mon 9/12/22	Mon 9/12/22	6	J&L Contractor							
8		Concrete Cure	7 days	Tue 9/13/22	Wed 9/21/22	7								
9		Design catwalk & ladder	11 days	Thu 8/25/22	Thu 9/8/22	3								
10		Cust Approval - Catwalk	1 day	Thu 8/25/22	Thu 8/25/22	4								
11		Order Material for catwalk and ladders	5 days	Fri 9/2/22	Thu 9/8/22	10FS+5 days								
12		Building Erection	9.5 days	Mon 11/7/22	Fri 11/18/22	8								
13		Unload Building	0.25 days	Mon 11/7/22	Mon 11/7/22									
14		Deliver Catwalk & Ladder Mater	1 day	Mon 11/7/22	Tue 11/8/22	13								
15		Red Iron Erection	3 days	Mon 11/7/22	Thu 11/10/22	13								
16		Wall Sheeting	2 days	Thu 11/10/22	Mon 11/14/22	15								
17		PBR Roof Sheeting	2.25 days	Mon 11/14/22	Wed 11/16/22	16								
18		Install Catwalk & ladders	0.75 days	Thu 11/17/22	Thu 11/17/22	17								
19		Install electrical	2 days	Wed 11/16/22	Fri 11/18/22	17FS-0.5 days	Electrical Contractor							
20		Gutter, Rake, & Downspouts	2 days	Thu 11/17/22	Fri 11/18/22	17								

Project: 22193_City of Nevada_
Date: Wed 8/24/22


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

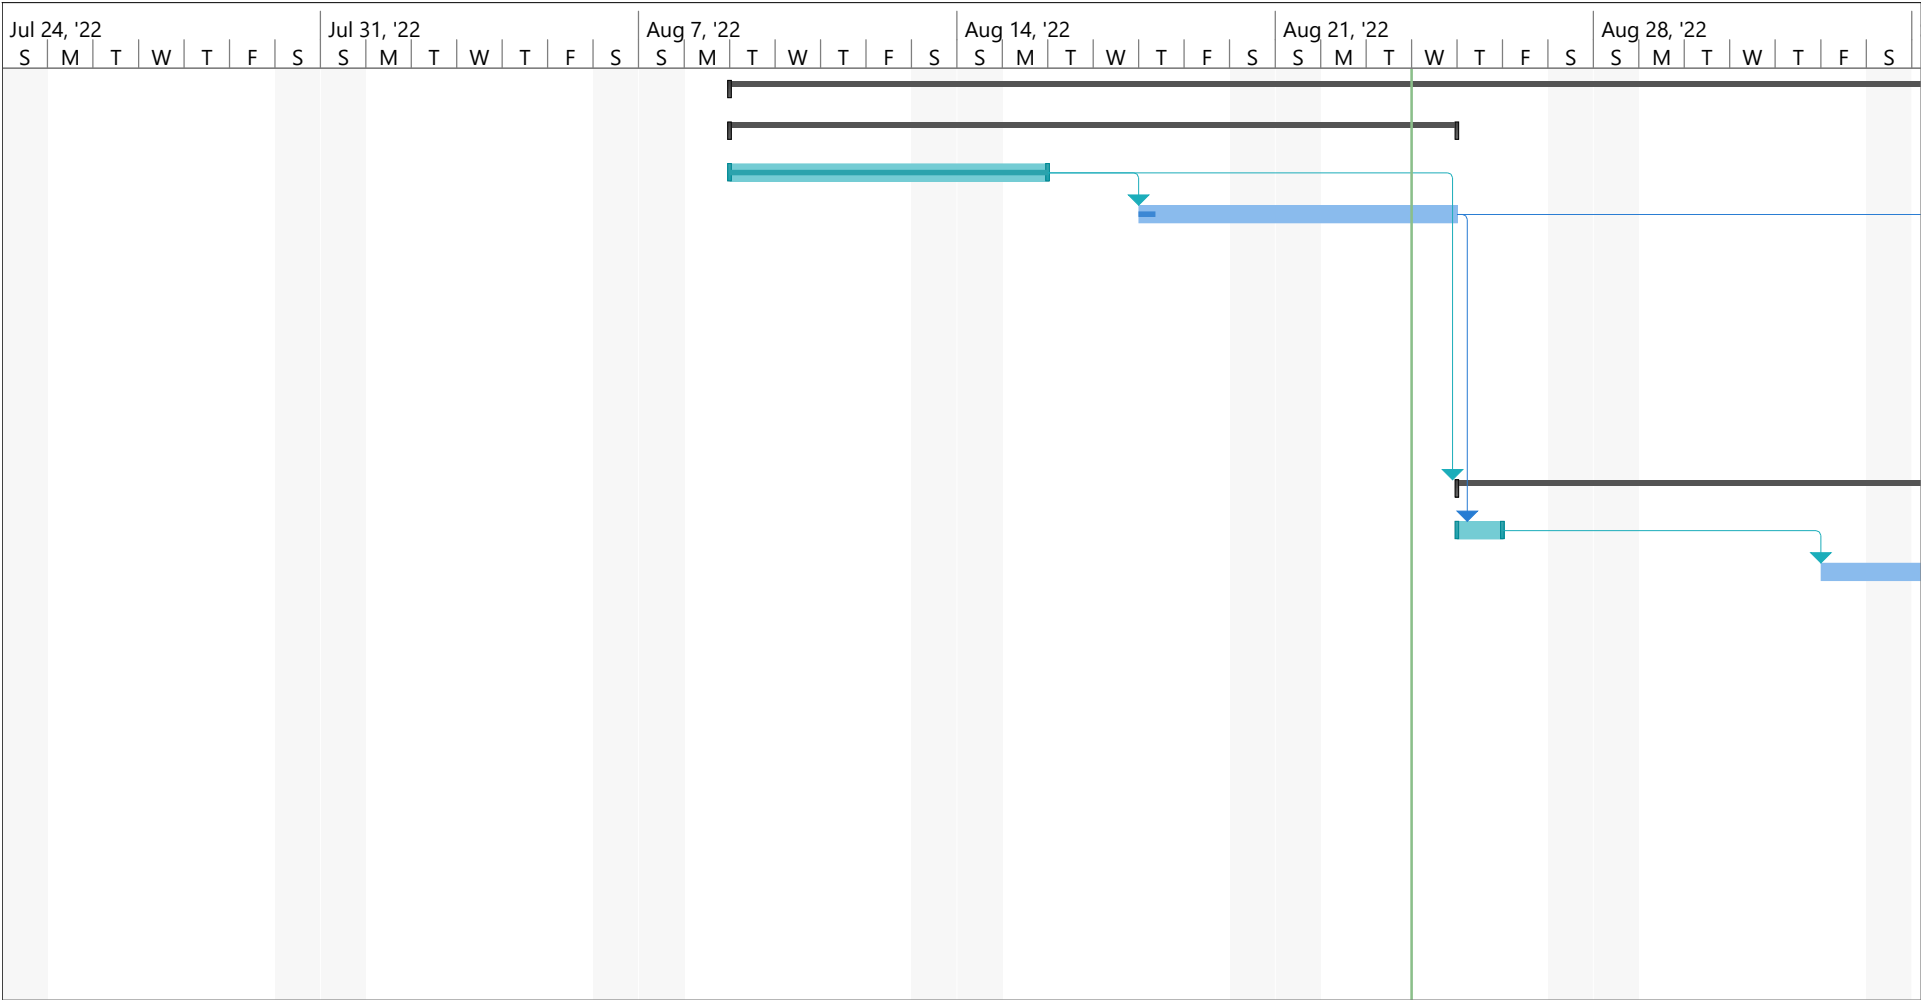

Project: 22193_City of Nevada_
Date: Wed 8/24/22

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


Sep 4, '22 Sep 11, '22 Sep 18, '22 Sep 25, '22 Oct 2, '22 Oct 9, '22

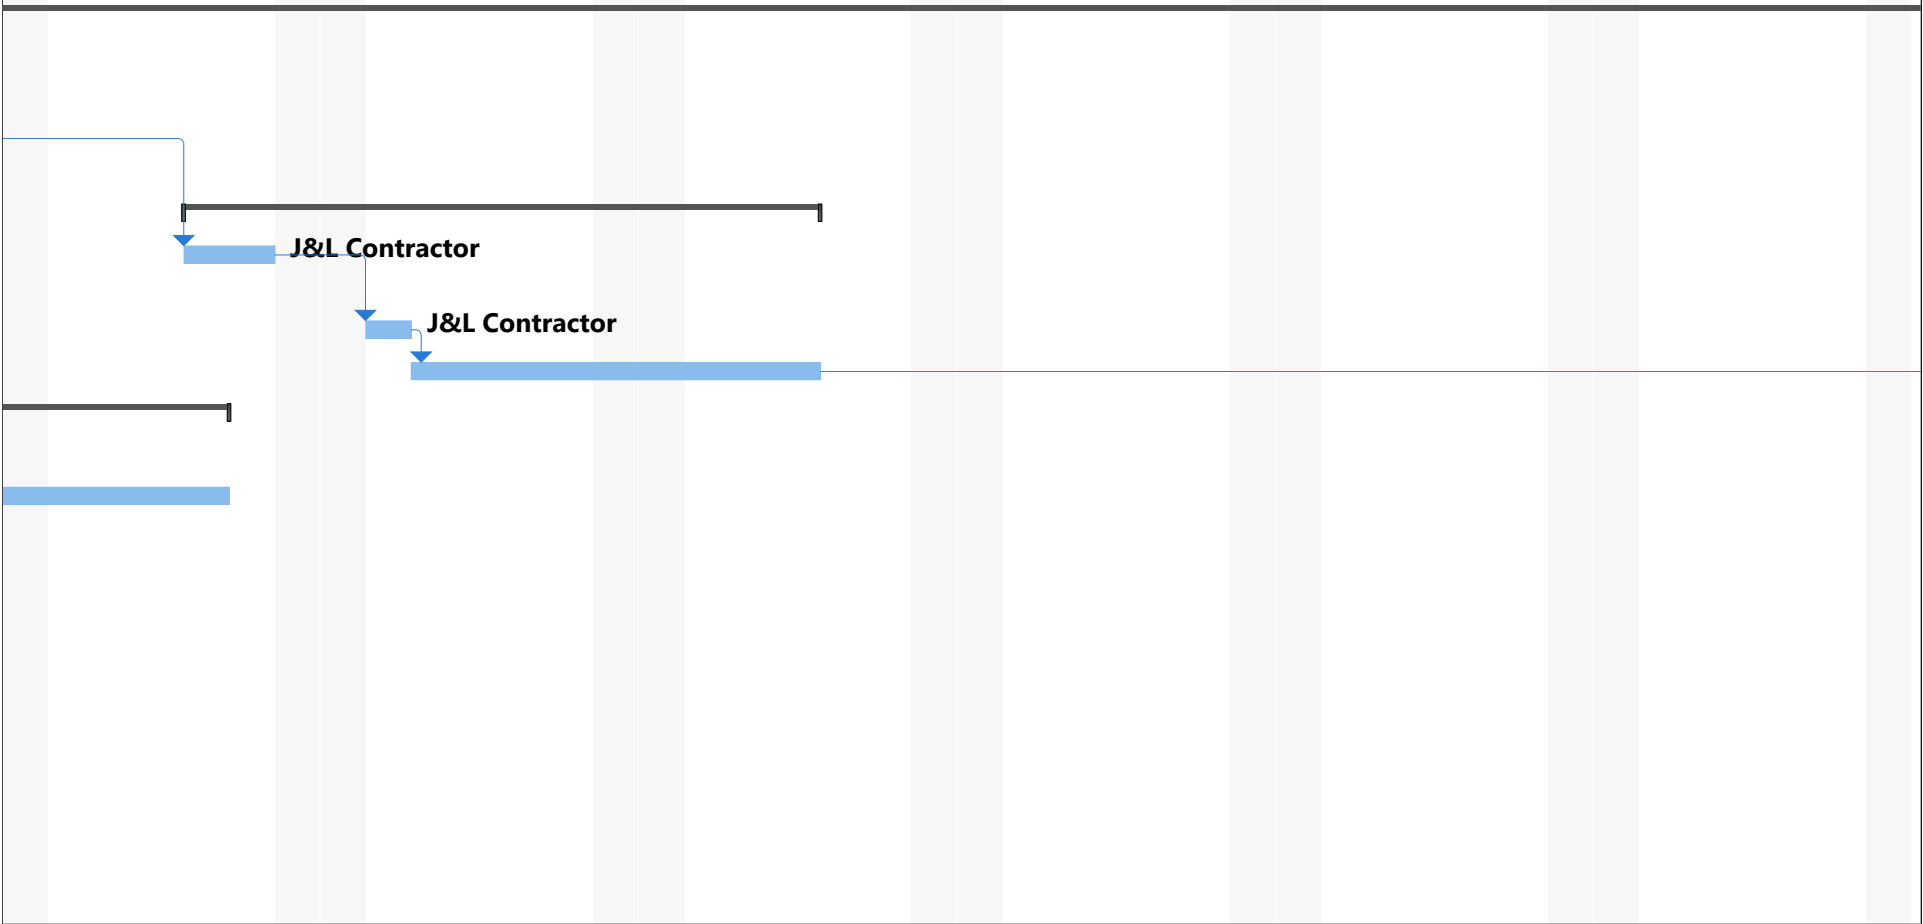

Project: 22193_City of Nevada_
Date: Wed 8/24/22

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Oct 16, '22 Oct 23, '22 Oct 30, '22 Nov 6, '22 Nov 13, '22 Nov 20, '22

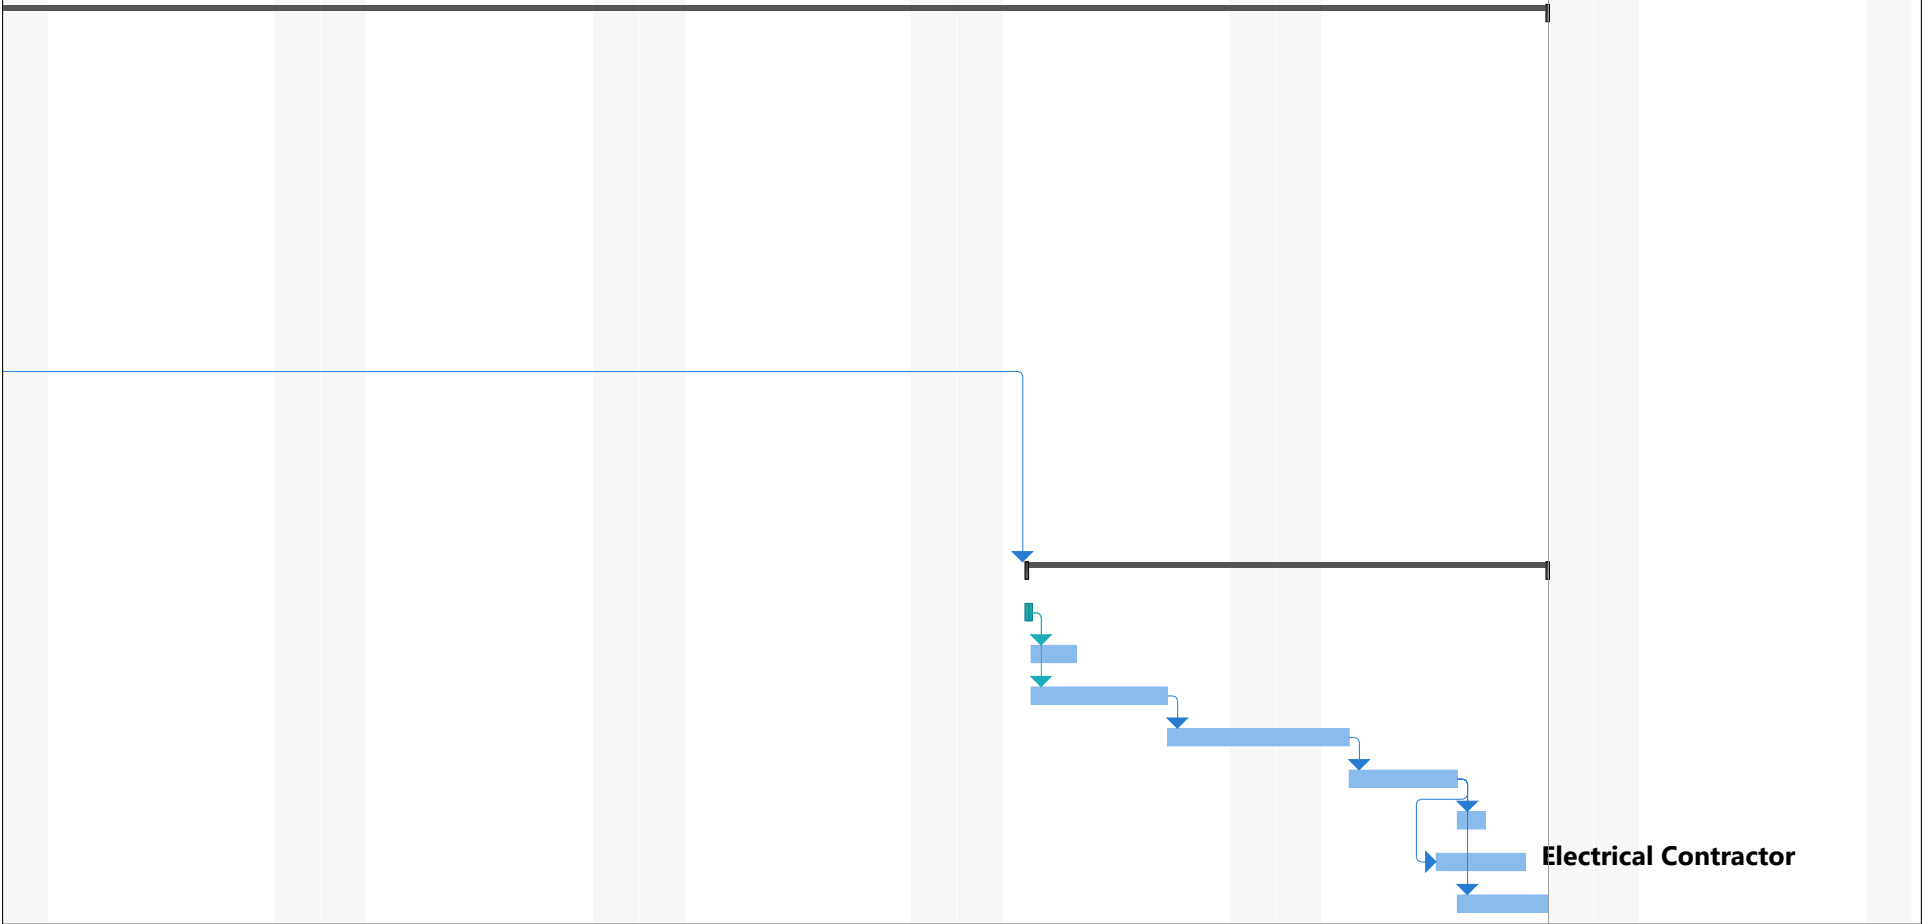

Project: 22193_City of Nevada_ Date: Wed 8/24/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
